


50/5*





Date: Wednesday, 06/08/2008 10:52:38 AM Melanie Fauteux User: **Process Sheet** Customer: CU-DAR001 Dart Helicopters Services Drawing Name: STABILIZER ARM Job Number: 41014 Part Number: PB674300157 Job Number: Seq. #: Machine Or Operation: Description: 7.0 240107 SPRING SLOTTED PIN Comment: Qty.: 2.0000 Each(s)/Unit Total: 10.0000 Each(s) 08-08-07 (5) SPRING SLOTTED PIN SMALL FAB 8.0 SMALL & MEDIUM FAB RESOURCE 1 Comment: 1- line drill -107 and -109 using existing pilot hole of -107 as per dwg 08-08-07 2- install spring pin 9.0 INSPECT WORK TO CURRENT STEP QC5 Comment: INSPECT WORK TO CURRENT STEP POWDER COATING 10.0 POWDER COATING M 102316 Comment: POWDER COATING Powder Coat Green Sandtex (Ref: 4.3.5.8) as per QSI 005 4.3 START TIME: OVEN TEMPERATURE: FINISH TIME: QC3 INSPECT POWDER COAT/CHEMICAL CONVERSION 11.0 Comment: INSPECT POWDER COAT/CHEMICAL CONVERSION PACKAGING PACKAGING RESOURCE # 12.0 39952 Comment: PACKAGING RESOURCE #1 Identify and Stock Location: FINAL INSPECTION/W/O RELEASE 13.0 QC21 0868/274 Comment: FINAL INSPECTION/W/O RELEASE U 08,08,26 Job Completion

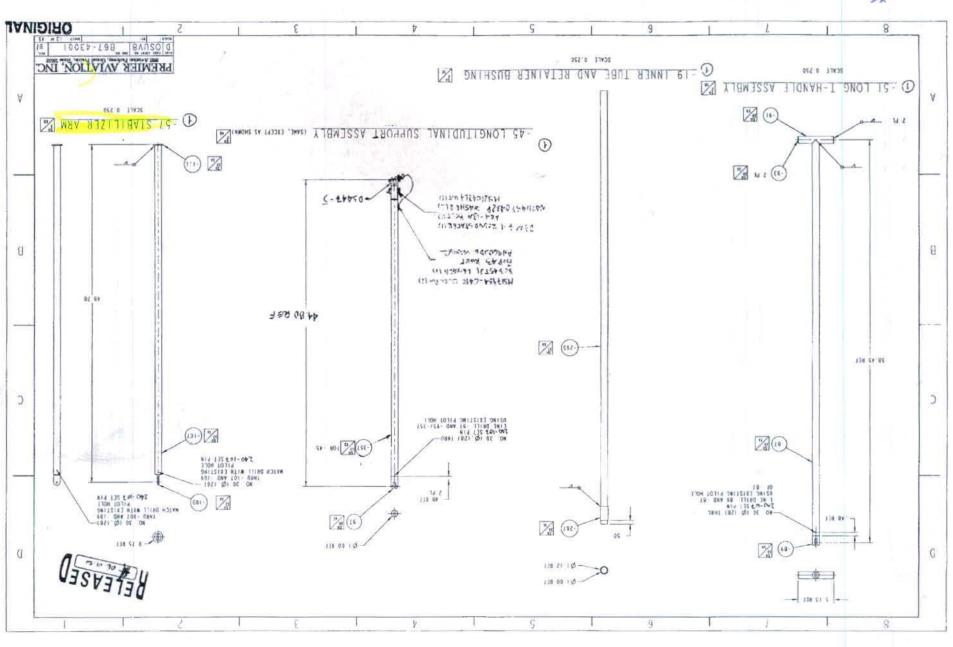

: STABILIZER ARM

: PB674300157

: 13/08/2008

: N/A

: B1

: B6743001 P.13

Wednesday, 06/08/2008 10:52:38 AM Oser:

Melanie Fauteux

Process Sheet

Drawing Name

Part Number

Material **Due Date**

Drawing Number

Project Number

Drawing Revision

Customer : CU-DAR001 Dart Helicopters Services

Job Number : 41014 **Estimate Number** : 13523

P.O. Number

This Issue : 06/08/2008

S.O. No. :

: NC Prsht Rev.

: 11 First Issue Previous Run

Checked & Approved By

Written By

Type

: SMALL /MED FAB

: Est Rev:A 08-07-25 new issue DD verified by:ec

Additional Product

Comment

Job Number:



Seq. #:

Machine Or Operation:

Description: Tube End Plate

PB6743001111



Comment: Qty.: 1.0000 Each(s)/Unit Total:

Tube End Plate

5.0000 Each(s)

batch: B 40013

PB6743001107

Comment: Qty.: 1.0000 Each(s)/Unit Total:

Tube Arm

5.0000 Each(s)

batch: 4/

4.0

LARGE FAB 1

Comment: LARGE FABRICATION RESOURCE 1

1-Weld assembly as per dwg PB67-43001

QC5



Comment: INSPECT WORK TO CURRENT STEP

5.0 QC9

Comment: VISUAL WELDING INSPECTION

PB6743001109 6.0

VISUAL WELDING INSPECTION

Male Eye





Comment: Qty.: 1.0000 Each(s)/Unit Total: 5.0000 Each(s)

Male Eye batch:

B40011
